

Implementation Plans for New Agreements

Board of Directors Meeting
August 27, 2026

Collection Agreement

Republic Services

- Re-Routing
 - Increase total number of routes from 76 to 86.5
 - Balance the collections/route/day to ensure 10-hour workdays
 - Task timeline May 2026 - October 2026
 - Approximately 30% of single-family homes will change collection days on March 1, 2027

Collection Agreement

Republic Services

- Notify customers of new collection days
 - Newsletter #1 - November 2026
 - Newsletter #2 – February 2027
 - Postcard #1 - First week of February 2027
 - Postcard #2 – Last week of February 2027
 - Phone call #1 – After last old collection day
 - Phone call #2 – Before 1st new collection day
 - Phone call #3 – Before 2nd new collection day
 - Email – In February 2027

Collection Agreement

Republic Services

- Purchase new vehicles

Truck Type	Ordered	Received	In Service
ASL	58	27	3
FEL	19	14	6
REL	5		
Burro	16		
Roll-Off	8		
Total	106	41	9



Collection Agreement Republic Services

Old Residential Trucks = Curotto Can



<https://youtu.be/hpGuMUq6e4Q?is=9uBLbCsY38ShBiNQ>

Collection Agreement

Republic Services

New Residential Trucks = Automated Side Loader



https://youtu.be/yYi2sAa0HU4?is=xEKtXCl1Vib2-Nr_

Collection Agreement

Republic Services

- Hire and train drivers
 - 119 drivers needed for our service area
 - 90 regular
 - 29 pool
 - Need to hire 14 additional drivers
 - Hiring process September – November 2026
 - Training current residential drivers on new ASL trucks
 - Began in June 2026
 - 14 drivers trained to date
 - 2 currently in training

Transfer Agreement


MDRR

- Update the Solid Waste Facility Permit (SWFP) and Transfer/Processing Report (TPR)
 - Current facility limit is 1,500 tons per day
 - Need an additional 500+ tons per day
 - Updating permit for 5,000 tons per day total
 - Submitted to CalRecycle on August 21, 2026
 - CalRecycle must respond by November 6, 2026
 - All other necessary permits acquired
 - CEQA review and public meetings complete

Transfer Agreement

MDRR

- Construction of new organics building
 - To be completed by end of October 2026.

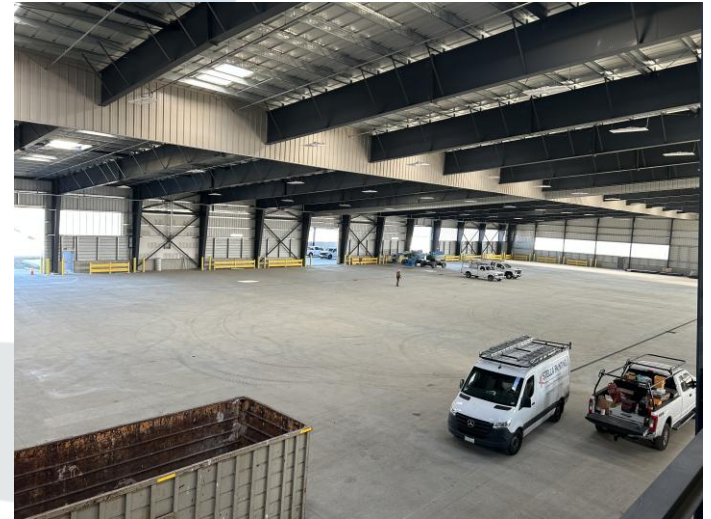

Transfer Agreement

MDRR

- Construction of new organics building
 - With load out tunnel



Transfer Agreement

MDRR

- Purchase new vehicles and equipment
 - 6 transfer trucks
 - 10 transfer trailers
 - 2 loaders
 - All received except for 1 loader expected in December



Transfer Agreement

MDRR

- Install 3 additional scales
 - Automated / unstaffed
 - Two inbound, one outbound
 - Delivered in September, operational by January
- Hire additional employees
 - 5 transfer drivers
 - 2 hostlers (on-site drivers)
 - 2 loader operators
 - 2 traffic control
 - Hiring process December - February

Recyclables Processing

MDRR


- Recyclables characterization study
 - Determine composition of the Authority's inbound, unprocessed recyclables
 - E.g. 10% of the inbound tons are cardboard
 - Measure the recovery rate of each commodity
 - E.g. MDRR can recover 95% of the inbound cardboard
 - Used to calculate recyclables revenue share
 - Study scheduled for September 12, 2026

Recyclables Processing

MDRR

- Be able to recover and market

- #5 plastic

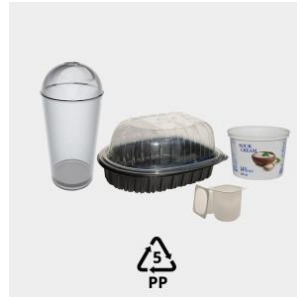

- #1 plastic thermoforms



Other Post-Collection Agreements

- The following agreements do not have significant implementation tasks:
 - Landfill disposal – Republic
 - Commer food scraps processing – Republic
 - Composting - Recology

Notable Authority

Implementation Tasks

- Add the community of Canyon
 - Currently Canyon residents have individual landfill carts and shared recycling bins



Notable Authority

Implementation Tasks

- Add the community of Canyon
 - Starting March 1, 2027
 - Canyon residents with sufficient space can request individual recycling and organic carts
 - Shared recycling bins will still be available to all Canyon residents
 - A shared organics bin will be placed next to the shared recycling bins, available to all
 - Canyon residents can subscribe to a 20-gallon landfill cart

Notable Authority

Implementation Tasks


- Add the community of Canyon
 - Not all Canyon residents have space for three carts
 - Authority to attend November 8 community meeting
 - Survey to determine who wants three carts



Notable Authority

Implementation Tasks

- New SB 1383 Compliance Software
 - Currently using “Recyclist” provided by Republic
 - In the new agreement the Authority will provide the SB 1383 Compliance Software
 - Software RFP
 - Issued August 28, 2026
 - Proposals due October 16, 2026
 - Review proposals October – November 2026
 - Approve agreement at February 2027 Board Meeting
 - May 1 – September 1, 2027 implementation
 - Overlap with “Recyclist” subscription



Questions

- Any implementation tasks of interest that weren't covered
- Level of detail desired
- Frequency of implementation plan updates to the Board
